

ARCHITECTURAL/STRUCTURAL


- Educational Needs Assessment and Programming are complete.
- Schematic Design is complete. All space layouts are designed/reviewed.
- Design Development is complete.
- Exterior building design/finishes is in progress.
- Construction Documentation is underway.
- Construction Cost is expected to increase due to inflation and supply chain issues. A revised estimate will be presented at the January Board Meeting.

CIVIL ENGINEERING, SITE PLANNING, APPROVALS

- Site Design is in progress.
- Sketch Plan was submitted to Jackson Township.
- Preliminary Plan was submitted to Jackson Township and reviewed.
- Review Comments are being addressed.
- Initial Design Submission has been sent to PennDOT.

PLUMBING/HVAC/ELECTRICAL ENGINEERING

- Access control meeting scheduled for 12/13/21.
- MEP review was provided for bi-weekly meeting on 12/20/21.

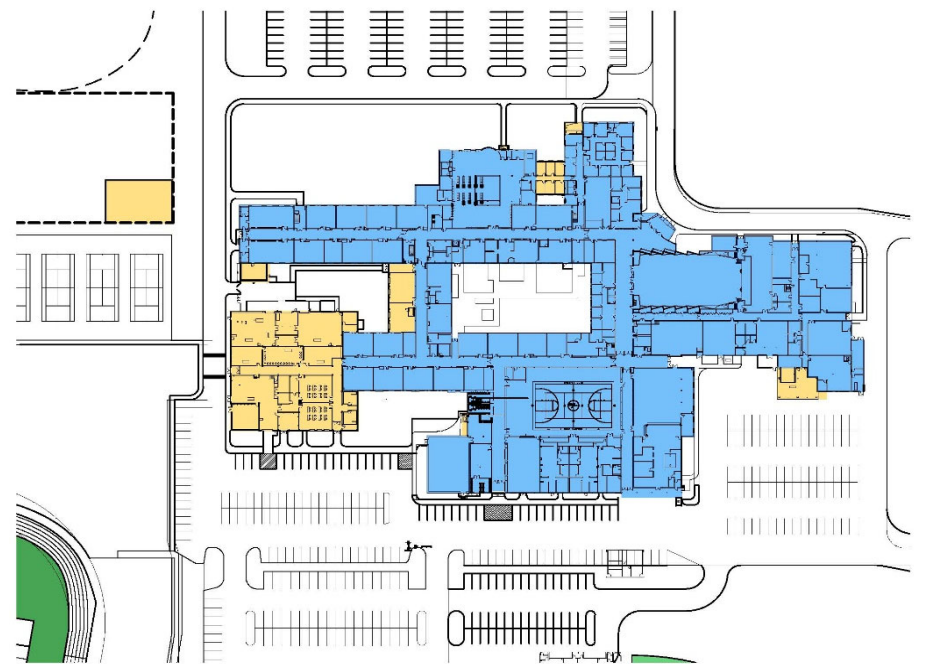

OWNER ACTION ITEMS

- Rebranding Initiative (Decisions may impact construction details.)
- ARP/ESSER Grant Submission

PROJECT SCHEDULE

	Start	Finish
Educational Planning & Schematic Design	11/1/2020	6/30/2021
Design Development	7/1/2021	10/31/2021
Construction Documentation	11/1/2021	2/28/2022
Land Development & Building Code Approvals	5/1/2021	2/7/2022
Board Authorizes Bidding		2/7/2022
Bidding Phase; Bids Received	2/28/2022	3/31/2022
Board Reviews Bids; Awards Contracts		4/6/2022
Execute Contracts, Begin Submittal Review		April 2022
First Day Contractors Are On-Site		May 2022
Phased Construction (Multiple Shifts)		27 Months
Final Date of Substantial Completion		July 2024
Final Phase Occupancy		August 2024

FINANCIAL INFORMATION TO BE ADDED

Proposed Administration Entrance



Proposed Gymnasium Main Entrance



Proposed Gymnasium Lobby

Proposed STEM Center Addition

